


Jahr 2020

Summe von kWh/kWp Monat	PV-Anlage					
	Josef	BvK	Walram	MCKG	Grevel	Deussenberg
1	24,41	26,43	22,18	19,39	19,29	21,26
2	35,59	37,94	33,19	37,34	35,75	37,85
3	95,78	101,73	91,18	108,49	99,38	107,22
4	140,95	152,45	141,22	154,97	144,16	151,81
5	145,29	158,45	150,50	157,05	156,45	143,41
6	121,30	136,09	128,77	134,86	136,66	133,68
7	112,89	129,20	122,60	124,60	124,28	123,86
8	105,51	119,66	114,35	123,80	122,10	124,26
9	89,12	99,66	92,81	105,77	104,69	106,51
10	39,43	43,04	38,98	46,31	35,87	43,41
11	38,08	40,61	34,68	37,34	25,77	41,62
12	15,27	16,56	10,44	12,82	8,84	16,28
Gesamtergebnis	963,62	1061,81	980,89	1062,74	1013,22	1051,18

prozentuale Abw. zu Josef-Schule

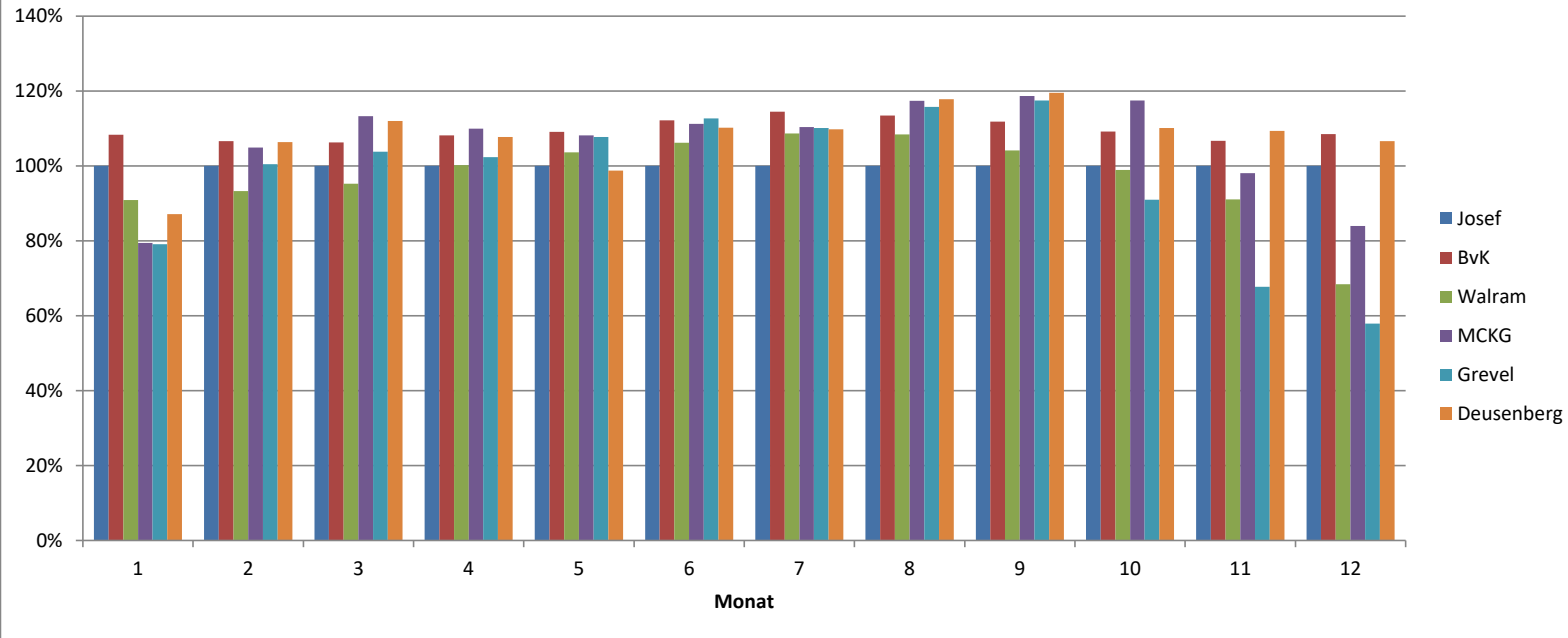

Jahr 2020

Monat	Josef	BvK	Walram	MCKG	Grevel	Deussenberg
1	100%	108,26%	90,85%	79,44%	79,03%	87,10%
2	100%	106,59%	93,26%	104,91%	100,45%	106,35%
3	100%	106,22%	95,20%	113,28%	103,76%	111,94%
4	100%	108,16%	100,19%	109,95%	102,28%	107,71%
5	100%	109,05%	103,58%	108,09%	107,68%	98,70%
6	100%	112,19%	106,15%	111,17%	112,66%	110,20%
7	100%	114,45%	108,60%	110,37%	110,09%	109,72%
8	100%	113,42%	108,38%	117,34%	115,72%	117,78%
9	100%	111,82%	104,13%	118,68%	117,46%	119,51%
10	100%	109,16%	98,87%	117,47%	90,97%	110,10%
11	100%	106,64%	91,07%	98,06%	67,67%	109,31%
12	100%	108,46%	68,36%	83,96%	57,89%	106,60%
Gesamtergebnis	100%	110,19%	101,79%	110,29%	105,15%	109,09%
